


**FDNY**  
**INCIDENT ACTION PLAN**  
**OPERATIONAL PERIOD**  
**OCTOBER 16 – 17, 2001**  
**0700 – 0700**

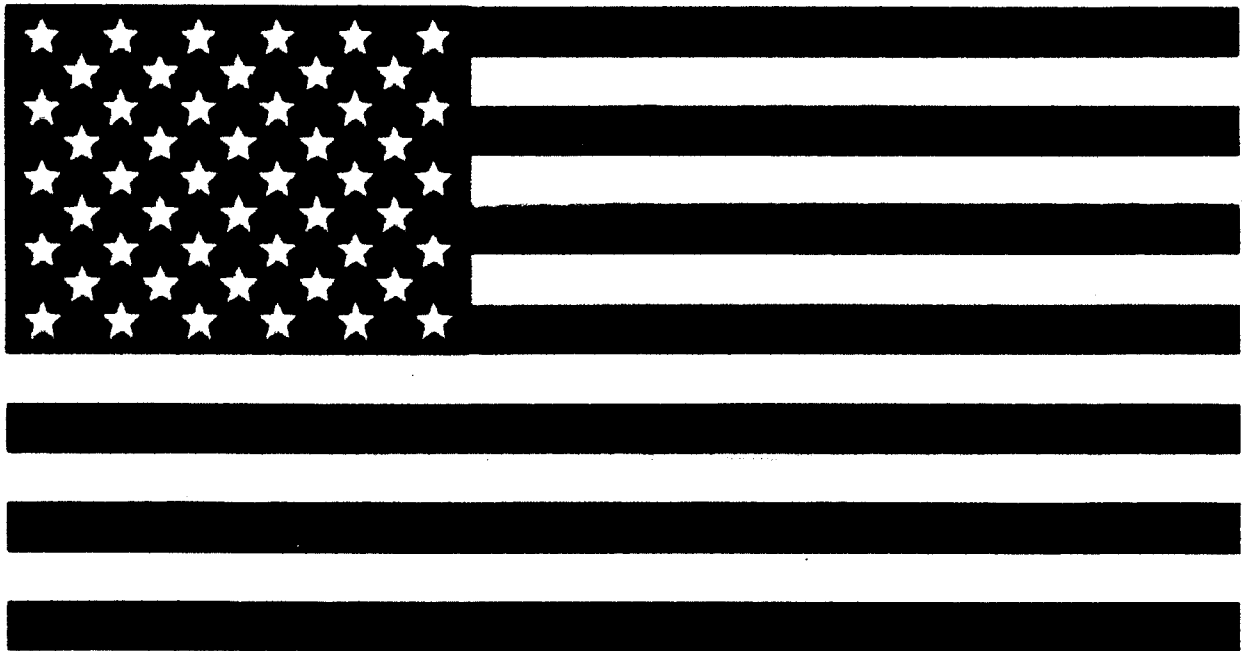

**PROUD TO BE AN  
AMERICAN**

*PH*

**OPERATIONAL PERIOD**

Tuesday 10/16/2001 – 0700 through Wednesday 10/17/2001 – 0700

**OVERALL INCIDENT OBJECTIVES**

1. Provide for the health, safety and welfare of all personnel working in and around the incident.
2. To provide for recovery and identification of as many remains as possible and return to next of kin.
3. Coordinate with all involved agencies to support the operational needs of the incident.
4. Document all critical items and significant events.

Each sector will have Planning and Documentation personnel assigned to support incident objectives. Specifically, they are tasked to update maps, track resource, record prior and current significant events, collect and record database requirements and provide liaison services at the request of Sector Chief. In addition, at the direction of the IC, other personnel will provide Incident Command System functional training to selected FDNY personnel.

**OPERATIONS FACILITIES AND LOCATIONS**

|                       |                                           |
|-----------------------|-------------------------------------------|
| Incident Command Post | 100 Duane Street                          |
| Operations Center     | 10/10 Station (Liberty & Greenwich)       |
| West Command          | Vesey & West (West & Liberty Sectors)     |
| East Command          | Liberty & Church (Church & Vesey Sectors) |

**OPERATIONAL RESOURCES**

|             |                                                                              |
|-------------|------------------------------------------------------------------------------|
| FDNY WTC TF | 160 (Total Firefighters/Officers) per 12-hour shift                          |
| NYPD ESU    | 50 Officers per 12 hour shift.                                               |
| PAPD        | 40 Officers per 12 hour shift.                                               |
| FEMA US&R   | 2 Technical Specialists to provide operational and planning support to FDNY. |
| DEP         | Emergency crew on stand-by at site for water main breaks – (917) 468-2877.   |
| ALASKA IMT  | 1 to 2 per Command to assist with planning and documentation.                |

**FDNY/EMS Staffing**

Each Sector will be staffed with the following minimum:

- One EMS Lieutenant
- One Gator with 2 EMT's
- One BLS Unit (Basic Life Support)

One ALS Unit (Advanced Life Support/Paramedic) at Liberty Sector Post

One ALS Unit (Advanced Life Support/Paramedic) at Vesey Sector Post

Disaster Medical Assistance Teams

Liberty Street / West Street (DMAT Medical Command and Pharmacy)

Fulton Street / Church Street

**WEATHER FORECAST**

**Day** Mostly Sunny, Winds E 10 mph, 0% chance of showers, Highs in the mid 60's.

**Night** Cloudy, Winds SW 10-15mph, 80% chance of showers, Lows in the 50's.

**Outlook** - Wednesday – Partly Sunny, 30% chance of showers, Highs in the lower 60's, Lows in upper 30's. Thursday – Mostly Sunny, Highs in the upper 50's with lows in the upper 40's.

Anemometer Locations: 11<sup>th</sup> floor of the Verizon Building, 3<sup>rd</sup> floor 10-10 Fire Station, 17<sup>th</sup> floor of 125 Liberty, 10<sup>th</sup> floor of 2 WFC, OEM Command Bus at West and Warren, East Command, and Federal Post Office.

### **ACCOMPLISHMENTS (Past 24 hours)**

1. Application of water to South Tower area and where heat and smoke are escaping in an attempt to extinguish/reduce the heat.
2. Operations continue on debris removal from the North Tower area with intermittent use of handlines to cool debris and for dust control.
3. Intermittent use of handlines in operation for dust control at 7 WTC.
4. Intermittent use of two multiversals in use for cooling and dust control between 5 & 6 WTC.
5. Continue to collect empty compressed gas cylinders.
6. Emphasis continues on slurry wall reinforcement in front of South Tower.
7. Steel and debris removal continues from core of South Tower. Handline is being used for dust control and cooling.
8. Revised guidelines for access to retrieve valuables have been completed.
9. Spill prevention and response plan has been submitted for review.
10. Contractor continues MTA debris removal on Church Street.
11. Identified and approved 4 zones (5 site) locations for compressed gas cylinder storage. (identified in Logistics page)

### **PLANNED ACTIONS (Next 24 hours)**

1. Steel cutting operations and subsequent removal of debris by rigging and heavy equipment will continue. Ironworkers are to be utilized to accomplish this mission. FDNY SOC and PD personnel will be utilized to assist and supplement this function. All available cutting set-ups should be utilized on a continual basis as conditions permit.
2. FD SOC personnel and PD personnel will continue to conduct void searches as required as heavy steel is removed.
3. All Emergency personnel operating on the South Tower in selected areas will be in bunker pants as needed.
4. Continue to place and use large caliber water streams for continuous fire extinguishment operations on 1 and 2 WTC as required. Place and use protective hand lines elsewhere as needed.
5. Continue to review operational/engineering plan to facilitate removal of the West façade walls still standing in the South Tower area. FDNY, DDC and site construction manager to review plan and evaluate results of deconstruction process.
6. Continue GPS mapping and documentation of recovery operations and structural features.
7. NIJ continues to operate five camera points for use in locating the flight recorders.
8. U.S. Army will continue laser mapping to detect any movement or shifting of piles. OEM is coordinating these activities.
9. Fire companies to wet down debris fields and dirt roads when requested by DDC.
10. DSNY will continue to water dusty streets and remove garbage.
11. Partial removal of west wall 2 WTC continues. (See attached Exclusion Zone diagram)
12. Entry into Chase Manhattan for retrieval of valuables.
13. Enter 4 WTC Bank of Nova Scotia at approximately 10:00 hours.

## **ANTICIPATED ACTIONS (72 hours)**

1. Continue in the planned actions and operating instructions.
2. As other crane(s) are set up and / or relocated, continue in the accelerated debris removal and void search operations. Concentration of operations will be in the following prioritized order as conditions permit:
  - Backfilling of slurry wall
  - North Tower (1 WTC)
  - North and West sides of Marriott
  - South Tower (2 WTC)
3. Perimeter security will continue and improve.
4. Review by Mayor's Office of the WTC Long Range Site Plan.
5. Establish guidelines for coordinated fueling services.
6. Initiate demolition of 3 southwest bays of 6 WTC.

## **SPECIAL INSTRUCTIONS**

1. **FDNY Sector Chiefs will approve all searches.**
2. **Follow the procedures identified in the attachment for retrieval of valuables from damaged structures.**
3. Review posted information regarding Minimum Protective Equipment Requirements, Site Safety, Evacuation Warning Signals, Site Hazards, Blood Borne Pathogens and Hazard Markings on Buildings.
4. For non-exempt personnel, only white, non-photo credentials will allow access into the site (Security checkpoints have a list of exempt agencies).
5. FDNY personnel arriving by bus from the Flushing Marina Staging area will be issued color-coded bands for authorized entry into the site. The colors for this operational period are as follows:

|          |           |              |
|----------|-----------|--------------|
| 10/16    | 0700-1100 | GLITTER PINK |
| 10/16    | 1100-2300 | BLACK        |
| 10/16-17 | 2300-0700 | KELLY GREEN  |

The band must be prominently displayed to allow entry onto the site.
6. GPS is to be used to plot locations of all victims, remains, fire equipment and apparatus. If the GPS is not operational, plot and record the location on the **grid map dated 09/20 or later**. GPS Units are available through the Sector Chiefs, who shall contact the GPS Team via channel 5.
7. When public safety personnel, apparatus and/or equipment are found, please protect the area and notify the appropriate agency for appropriate documentation and removal. If **weapons or ammunition** are found, secure the area and immediately notify law enforcement authorities.
8. There are two small residential type safes in the canine area on B-1 of 2 WTC, which contain explosive materials used for training dogs. The pile of debris is now ten feet above grade but as pile is reduced to grade level operations in this location must be coordinated with PAPD and NYPD.
9. Damaged SCBA Tanks:
  - a. If possible, slowly remove air pressure by opening valve.
  - b. If the valve is damaged or missing – do not remove tank and notify Sector Chief.
  - c. Sector Chief will notify Operations Command Post for relay to HazMat Operations for further instructions.
10. Enclosures on North and South projections on West Street are locked. The keys will be located with the FDNY Command Post, NYPD Officer at enclosure and OEM.
11. A single unit with one fire officer and 2 firefighters is dedicated to initial response to fires and emergencies within the restricted area dispatched through Manhattan CO.
12. NYPD will have K-9's available at 1 and 2 WTC's, the Marriott Hotel and the Plaza for use when excavators are not operating.
13. **No open flames or warming fires.** Use the warming tents if necessary.
14. **No parking along Church between Liberty and Vesey.**
15. All personnel are to remain outside the exclusion zone west of the West wall of Tower 2, which will be marked, until the 8 sections are removed. (See Diagram)
16. Oxygen tube trailer movements (incoming or repositioning) require notification of FDNY Sector Chief.

# DEPARTMENT OF DESIGN AND CONSTRUCTION UPDATE

## ACCOMPLISHMENTS (Past 24 hours)

1. Road construction of the South to East Road East of the South Tower (2 WTC) continues as debris is removed.
2. Operations continue on debris removal from the North Tower area with occasional use of multiversal to cool debris.
3. Dewatering commenced on Liberty Street and well drilling is continuing along Liberty & West streets.
4. Test borings completed on Liberty Street.
5. First phase of crane matting at 6 WTC is complete.
6. Contractor completed MTA debris removal and maintenance of traffic on Church Street BMT.
7. Operations west of the West wall of Tower 2 is on hold and a safety zone has been established (See Diagram).
8. Demolition of southwest bays of 6 WTC has commenced.
9. Shoring for roadway between 4 & 5 WTC completed.

## PLANNED ACTIONS (24 hours)

1. Demolition of southwest bays of 6 WTC for crane access to north façade of 1 WTC.
2. Continuing access road construction to Plaza.
3. Continue to backfill void North of slurry wall & South of 2 WTC from Greenwich to West Street to be completed 10/19/01. Two conveyors are set up to expedite progress.
4. Well points being installed on Liberty Street and also West Street by Moretrench Drilling.
5. Continue to shore floors at 3 WTC that will take 2 weeks.
6. Movement of 550 Grappler for 6 WTC demolition.
7. Removal of 2 WTC south and west façades to continue.
8. Pull down 8 northwest columns of 2 WTC facade steel. (See Diagram)
9. DDC will provide an overall site project plan on 10/15/01.
10. Contractor to continue MTA debris removal and management of traffic on Church Street.
11. Removal of steel from Bankers Trust.
12. Debris removal plaza area of 5 WTC.
13. Core drilling of east to west slurry wall south of 2 WTC.

## ANTICIPATED ACTIONS (72 hours)

1. Test borings and well points to be installed on Liberty and West Streets to be continued.
2. Start installation of tie - rods on Liberty Street (Tuesday 10/16/01).
3. Second phase of matting at 6 WTC for access to North façade of 1 WTC for demolition.
4. DDC and FDNY will meet Wednesday at 13:30 at Duane St. Command Post to discuss the sequence of operations and perimeter map.
5. Core drilling of east to west slurry wall south of 2 WTC.
6. Debris removal north and west of the Marriott (Vista) hotel.
7. Construction of north to south retaining wall for BMT on Westside of Church Street.

There is an OEM representative located at the OEM trailer (Murray and West - 212 941-5337) to contact DDC to handle contractor problems.

To contact the contractors on site, DDC has a person stationed at 10/10 to assist.

OEM is also the contact for OSHA.

10/16/01

FDNY IAP - NOT FOR PUBLIC DISTRIBUTION

100- west command

## LOGISTICS

Access points are as follows:

- |                                   |                               |
|-----------------------------------|-------------------------------|
| • West & Chambers                 | Vehicle and Pedestrian access |
| • Church & Chambers               | Vehicle and Pedestrian access |
| • Murray & Broadway               | Vehicle access only           |
| • Trinity Place & Rector          | Vehicle access only           |
| • Carlisle Street (West) & Rector | Vehicle and Pedestrian access |

Meal Sites are as follows:

- St. John University at 101 Murray
- Marriott WFC Hotel, Albany & West.

Water and Snack Sites are:

- West & Murray
- Church & Dey

Sanitation Sites are as follows:

- Personal hygiene stations are in place on Liberty, between Church & Greenwich.
- Personal Hand Washing Stations are available at all the above meal sites.
- Boot washes; hand & eye wash stations at West & Murray, St. Johns Univ. also West & Rector.
- Additional washes and showers are available on a limited basis at the Liberty Street Marina to augment the entrance / exit facilities.

Cache Sites (PNW – IMT) are as follows: **Supplies are for uniformed emergency personnel only.**

**Contractors must provide for their own personnel.**

- West Sector – On West Street just north of Vesey Intersection.
- Liberty Sector – Ground floor of 1 WFC.
- Church Sector – At Liberty & Church.

Vehicle Wash Sites are as follows:

- |                                |                           |
|--------------------------------|---------------------------|
| • Southend Ave. and Albany St. | • Rector and Greenwich.   |
| • West St. South of Albany St. | • Park Place and Church.  |
|                                | • West St. and Warren St. |

Coveralls will only be available at the World's Fair Marina (WFM).

Respirators – fitted and issued by EMS personnel at WFM. Respirators are available at cache sites and IS 89. Goggles and gloves are available through the cache system.

Staffing: DC report at 0700 and 1900 directly to the Ops Post at 10-10.

BC and FF report at 0930 and 2130 to WFM.

Transition to the West and East Command Posts is complete.

### WEST COMMAND POST

212-608-7753  
212-608-7754  
212-608-7796  
212-608-8048  
212-608-9556 fax  
212-608-9801 fax

### EAST COMMAND POST

212-425-4201  
212-425-4231  
212-425-4217  
212-425-4180  
212-425-4221  
212-425-4096 fax

Approved Compressed Gas Storage Locations: Note: Sites, although approved, are subject to change.

- AMEC Zone: West Street adjacent to foundation for North Bridge
- BOVIS Zone: Inside fenced turnout in front of 1 WFC. Fence to be raised to 16 feet.
- TULLY Zone: South side of Liberty Street between Broadway and Church.
- TURNER Zone: Greenwich Street between Park Place and Barclay
- Corner of Vesey and West Broadway.

Two sites approved in Turner zone due to restricted access configuration.

Additional safety requirements will be implemented as needed.

**Safety Message**  
**10/16/01**



**Major Hazards:**

**Crane Operations**  
**Demolition Operations**  
**Biological Hazards**

**Falling Glass & Debris**  
**Traffic**  
**Walking and Working Surfaces**

**Hazardous Materials**  
**Lack of PPE**  
**Dust and Airborne Particles**

**⇒ PPE\*** is designed to help protect you from injury. It doesn't work unless you use it.

**\*Hard Hat - Eye Protection - Respirators –**

**⇒ O<sub>2</sub> Tube Trucks** are a significant risk. Operators and personnel must use caution whenever working around them. All tube trucks should be guarded by a barrier, and situated away from high traffic areas.

**⇒ Traffic** is a continual problem. Space at the site is in short supply. If you don't need to drive into the area, don't.


**⇒ Watch** for falling debris around working equipment or when walking near buildings at the site.

Heavy equipment, such as backhoe or grapple, working within 50' of O<sub>2</sub> tube trailers shall have a Safety Officer to supervise all movements of equipment and ensure safety of personnel.

**“Safety—It's a way of Life ”**

10/16/01

# FDNY – WTC ORGANIZATIONAL CHART

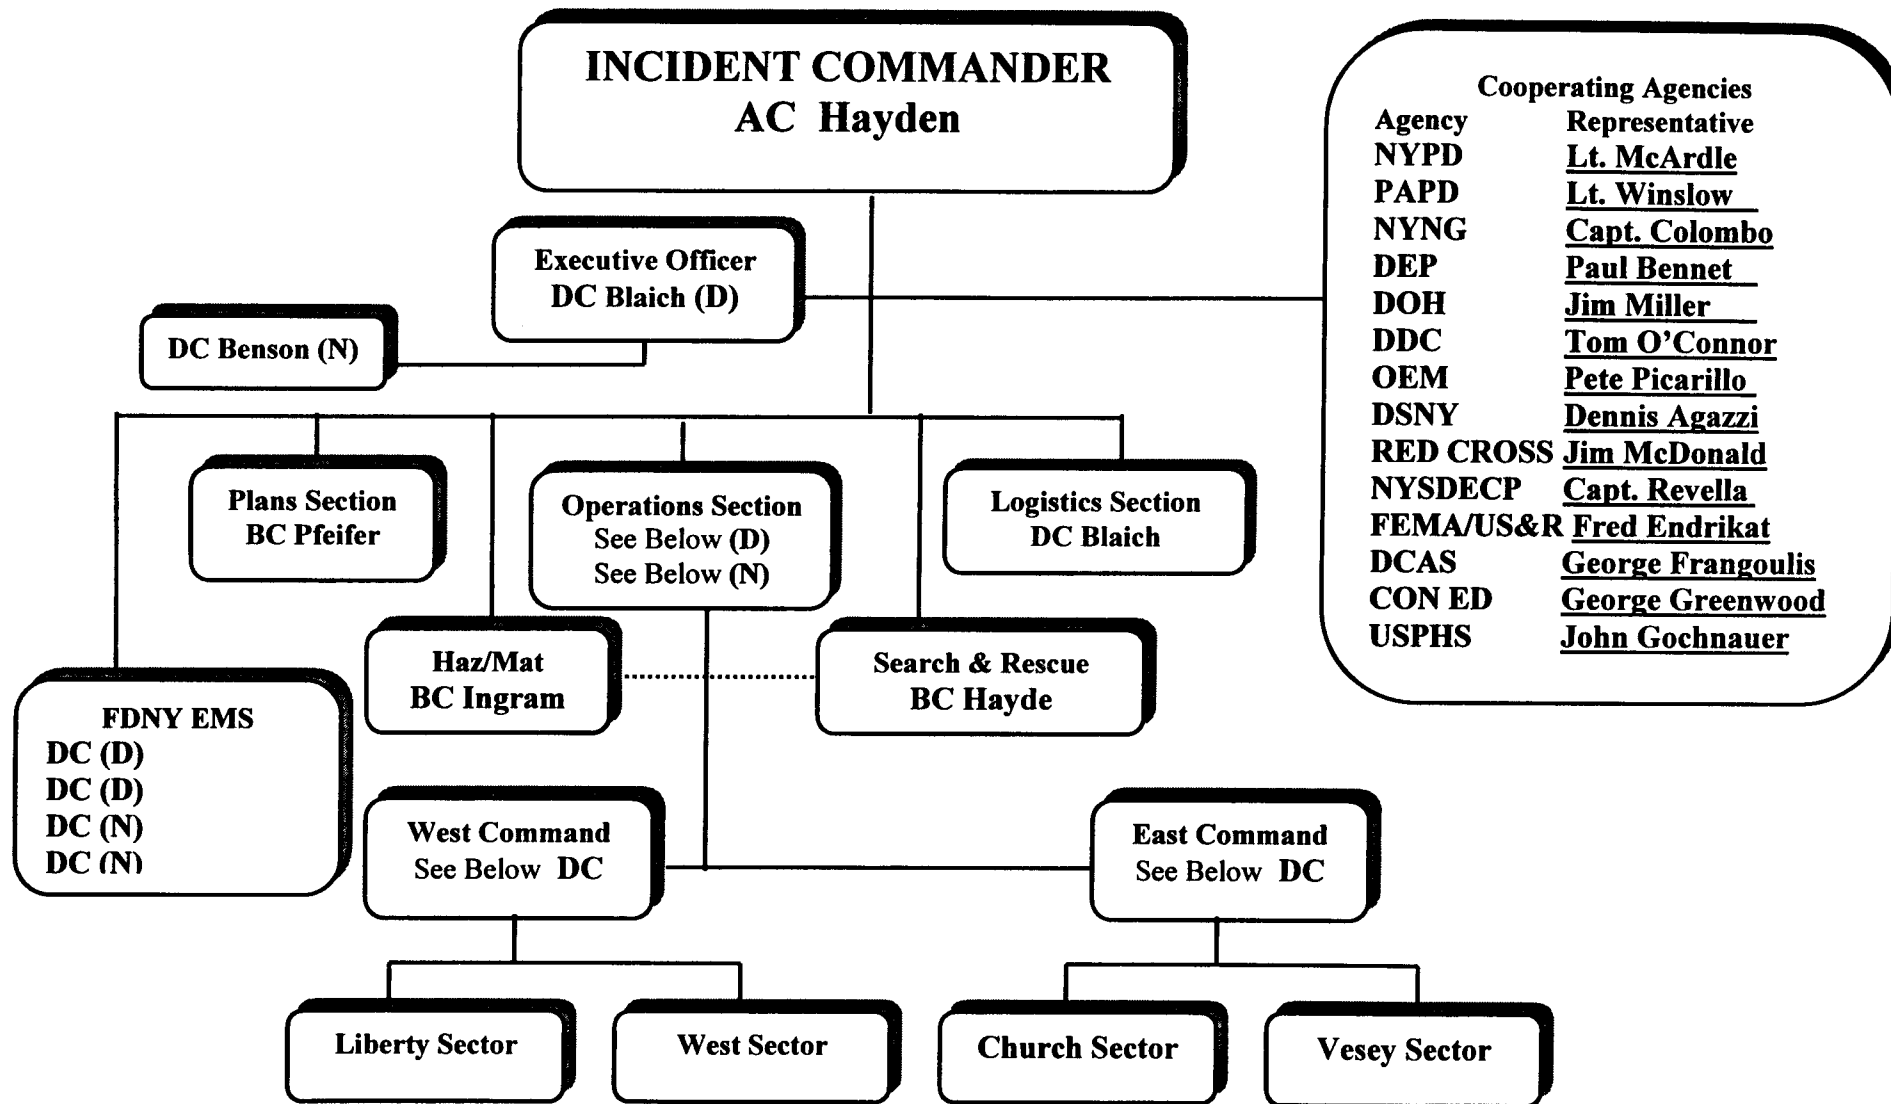


|                |        |     |             |              |                  |             |              |
|----------------|--------|-----|-------------|--------------|------------------|-------------|--------------|
| WTC Task Force | Tour 1 | (D) | 0700 – 1900 | 10/15        | Operations Chief | AC – Callan | DC - Hay     |
|                | Tour 2 | (N) | 1900 - 0700 | 10/15 –10/16 | Operations Chief | AC -        | DC - Jackson |
|                |        |     |             |              |                  |             | DC -         |
|                |        |     |             |              |                  |             | DC -         |

**10/15/01****FDNY – WTC ORGANIZATIONAL LIST**

|               |                                                    |                                                              |
|---------------|----------------------------------------------------|--------------------------------------------------------------|
| FDNY          | Duane St. Command Post                             | 646-613-0228/1591/7293                                       |
| NYPD          | Lt. McArdle                                        | 212-227-0010 or 212-227-5564<br>Pager 914-771-2889           |
| PAPD          | Lt. Mark Winslow                                   | 212-941-5252                                                 |
| OEM           | Pete Picarillo (LOGS)<br>Kevin Culley (IC Liaison) | 646-210-5861 or 646-756-3018<br>202-297-7680                 |
| DEP           | Tom DePrisco<br>Paul Bennet or acting              | 646-756-6332 or 347-203-4177 (Cell)<br>917-468-2877          |
| DDC 0500-1400 | Tom O'Connor                                       | 917-560-5365                                                 |
|               | Tom Amoia                                          | 917-681-7572                                                 |
|               | Ed McGinley                                        | 347-245-0387                                                 |
| 1300-2200     | Lou Mendes                                         | 646-235-3394                                                 |
|               | Joe Deluca                                         | 347-386-7329                                                 |
| 2100-0600     | Charlie Kaczorowski                                | 646-772-2406                                                 |
| DOH           | Dr. Jim Miller                                     | 917-642-2809                                                 |
| NYSDECP       | Capt. T. Revella                                   | 646-756-3136                                                 |
| DSNY          | Dennis Agazzi                                      | 646-235-3000                                                 |
| RED CROSS     | Jim McDonald                                       | 703-728-8574 or 718-923-1432                                 |
| ROBOTICS      | Arnis Mangolds<br>Bob Guelli                       | 617-306-5709 or 781-684-4379<br>617-921-2464 or 781-684-4332 |
| NYCSO         | Lt. Scali                                          | 646-756-3125                                                 |
| NYNG          | Capt. Colombo<br>Lt. Erazo                         | 973-615-6219 or 212-941-5281<br>917-577-2136                 |
| FEMA/US&R     | Fred Endrikat                                      | 917-709-3118                                                 |
| DCAS          | George Frangoulis                                  | 646-772-8158                                                 |
| CON ED        | George Greenwood                                   | 212-460-2602                                                 |
| USPHS         | John Gochnauer                                     | 347-231-4523                                                 |

# Exclusion Zone for Removal of 2 WTC Facade – Monday Night - Tuesday

Section of  
unsafe wall to  
be removed.

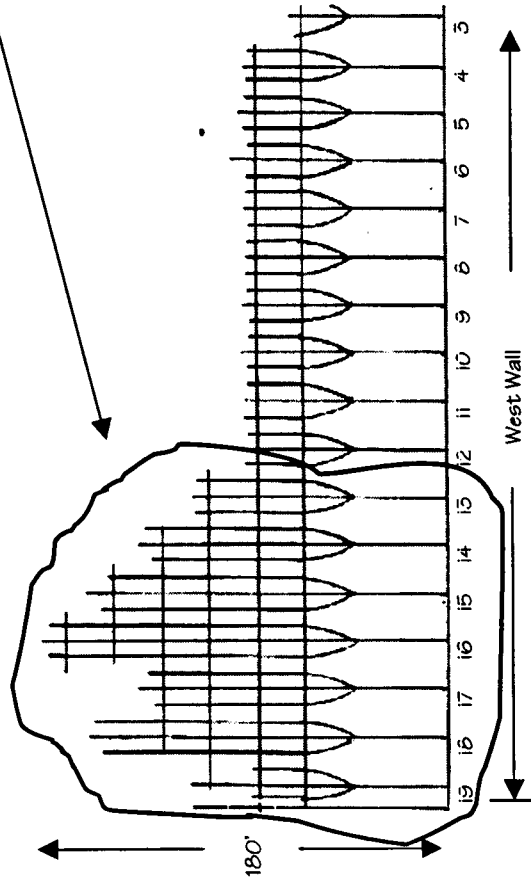


Exclusion Zone is west of 2 WTC northwest corner. Zone will be marked for personnel exclusion until the eight columns are removed.

## **Requests For Access To Retrieve Valuables From Damaged Structures**

1. Have person making request contact Capt. (PD) Tom DePrisco at OEM 646-756-6332 or 347-203-4177. Capt. DePrisco will verify the person's I.D. and authorization to enter area. After this is complete, he will forward authorization info to us for scheduling of entry.
2. After authorization is received, contact the party to schedule a time. (Record here) contact PAPD Lt. Winslow to have a team videotape recovery (212) 941-5252.
3. Send a FD-SOC representative (FF O'Connell if available) to survey the site for structural stability and site hazards. FD will determine whether or not area can safely be entered and if work can be carried out.
4. Notify ESU CP (Lt. McArdle if available) for the need for a team to accompany extremely valuable removals.
5. Entries should only be permitted to reclaim cash or bonds or other highly valuable, relatively irreplaceable goods. No entries will be permitted to retrieve personal effects.



# DR-1391-NY New York City Facility Locations - October 15

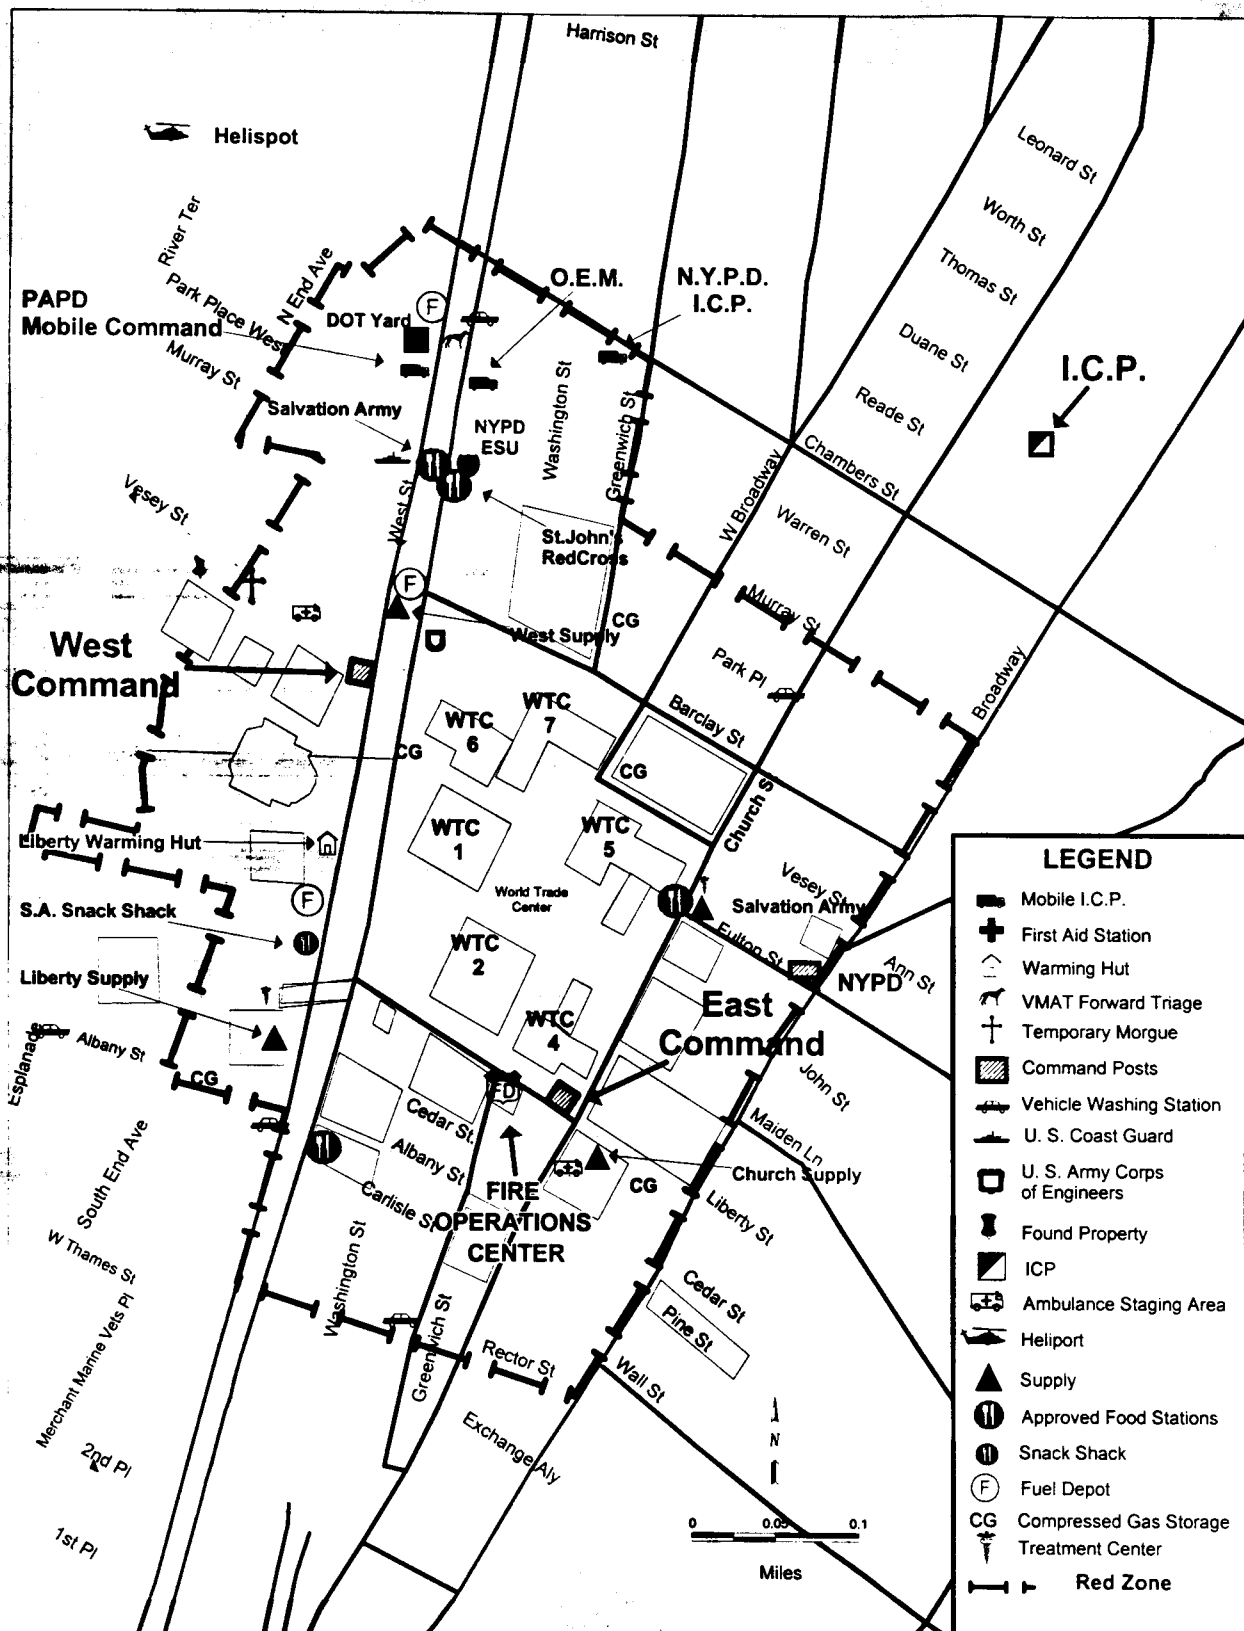

map #1



FEMA GIS DR 1391 NY  
IST Situation Unit  
printed on 10-15-2001 RK  
Facility Locations 10.15.wor



## Current Conditions, Forecasts, Watches and Warnings for New York (Manhattan), NY

- [Current Conditions in New York](#)
- [Zone Forecast for New York \(Manhattan\), NY](#)
- [State Forecast for New York](#)
- [Area Conditions for New York \(Manhattan\), NY](#)

---

### Zone Forecast for New York (Manhattan), NY

[↑ Top of page](#)   [↑ Table of contents for New York \(Manhattan\), NY](#)

FPUS51 KOKX 160801

ZFPKX

#### ZONE (COUNTY) FORECASTS

NATIONAL WEATHER SERVICE NEW YORK NY

401 AM EDT TUE OCT 16 2001

NJZ005-006-011-NYZ072>077-162201-

BRONX-ESSEX-HUDSON-KINGS (BROOKLYN)-NASSAU-NEW YORK (MANHATTAN)-

QUEENS-RICHMOND (STATEN ISLAND)-UNION-

401 AM EDT TUE OCT 16 2001

#### TODAY

MOSTLY SUNNY THROUGH EARLY AFTERNOON...THEN INCREASING CLOUDS. HIGHS IN THE MID 60S. EAST WIND 5 TO 10 MPH BECOMING SOUTHEAST 10 TO 15 MPH THIS AFTERNOON.

#### TONIGHT

OCCASIONAL SHOWERS WITH A CHANCE OF A THUNDERSTORM...ENDING AFTER MIDNIGHT. LOWS IN THE LOWER 50S. SOUTHEAST WIND 10 TO 15 MPH BECOMING WEST AFTER MIDNIGHT. CHANCE OF RAIN 80 PERCENT.

#### WEDNESDAY

PARTLY SUNNY AND WINDY. HIGHS IN THE LOWER 60S. WEST WIND 20 TO 25 MPH AND GUSTY.

#### WEDNESDAY NIGHT

MOSTLY CLEAR. LOWS IN THE LOWER 40S.

#### THURSDAY

MOSTLY SUNNY. HIGHS NEAR 60.

#### THURSDAY NIGHT

MOSTLY CLEAR. LOWS IN THE UPPER 40S.

#### FRIDAY

MOSTLY CLEAR. HIGHS IN THE MID 60S.

**SATURDAY**

PARTLY CLOUDY. LOWS IN THE MID 50S AND HIGHS IN THE MID 60S.

**SUNDAY**

MOSTLY CLEAR. LOWS IN THE MID 50S AND HIGHS IN THE MID 60S.

**MONDAY**

PARTLY CLOUDY. LOWS IN THE MID 50S AND HIGHS IN THE MID 60S.

---

**State Forecast for New York**

[↑ Top of page](#)   [↑ Table of contents for New York \(Manhattan\). NY](#)

FPUS61 KOKX 160804  
SFPNY  
NYZ067>081-162304-

**TABULAR STATE FORECAST FOR EXTREME SOUTHEAST NEW YORK**  
**NATIONAL WEATHER SERVICE NEW YORK NY**  
**404 AM EDT TUE OCT 16 2001**

ROWS INCLUDE...

DAILY PREDOMINANT DAYTIME WEATHER  
FORECAST TEMPERATURES...DAYTIME HIGH...NIGHTTIME LOW  
- INDICATES TEMPERATURES BELOW ZERO  
DAYTIME PROBABILITY OF PRECIPITATION  
-- INDICATES MISSING VALUES

| FCST   | FCST   | FCST   | FCST   | FCST   | FCST   | FCST   |
|--------|--------|--------|--------|--------|--------|--------|
| TUE    | WED    | THU    | FRI    | SAT    | SUN    | MON    |
| OCT 16 | OCT 17 | OCT 18 | OCT 19 | OCT 20 | OCT 21 | OCT 22 |

**CITY****LONG ISLAND****FARMINGDALE**

|        |        |       |       |       |       |       |
|--------|--------|-------|-------|-------|-------|-------|
| PTCLDY | PTCLDY | SUNNY | SUNNY | SUNNY | SUNNY | SUNNY |
| 64/52  | 62/40  | 60/48 | 65/55 | 65/54 | 65/54 | 65    |
| POP 0  | POP 0  | POP 0 | POP 0 | POP 0 | POP 0 | POP 0 |

**ISLIP**

|       |        |       |       |       |       |       |
|-------|--------|-------|-------|-------|-------|-------|
| SUNNY | PTCLDY | SUNNY | SUNNY | SUNNY | SUNNY | SUNNY |
| 64/52 | 62/39  | 59/43 | 63/51 | 63/50 | 63/49 | 62    |
| POP 0 | POP 0  | POP 0 | POP 0 | POP 0 | POP 0 | POP 0 |

**WESTHAMPTON**

|       |        |       |       |       |       |       |
|-------|--------|-------|-------|-------|-------|-------|
| SUNNY | PTCLDY | SUNNY | SUNNY | SUNNY | SUNNY | SUNNY |
| 64/52 | 62/38  | 59/43 | 63/51 | 63/50 | 63/49 | 62    |
| POP 0 | POP 0  | POP 0 | POP 0 | POP 0 | POP 0 | POP 0 |

**LOWER HUDSON VALLEY****MONTGOMERY**

|        |        |       |       |       |       |       |
|--------|--------|-------|-------|-------|-------|-------|
| PTCLDY | MOCLDY | SUNNY | SUNNY | SUNNY | SUNNY | SUNNY |
|--------|--------|-------|-------|-------|-------|-------|

|       |        |       |       |       |       |       |
|-------|--------|-------|-------|-------|-------|-------|
| 62/47 | 58/33  | 58/40 | 61/46 | 60/45 | 62/45 | 63    |
| POP 0 | POP 10 | POP 0 | POP 0 | POP 0 | POP 0 | POP 0 |

## WHITE PLAINS

|        |        |       |       |       |       |       |
|--------|--------|-------|-------|-------|-------|-------|
| PTCLDY | PTCLDY | SUNNY | SUNNY | SUNNY | SUNNY | SUNNY |
| 63/50  | 60/37  | 59/44 | 63/50 | 62/50 | 63/51 | 64    |
| POP 0  | POP 10 | POP 0 | POP 0 | POP 0 | POP 0 | POP 0 |

## NEW YORK CITY

## CENTRAL PARK

|        |        |       |       |       |       |       |
|--------|--------|-------|-------|-------|-------|-------|
| PTCLDY | PTCLDY | SUNNY | SUNNY | SUNNY | SUNNY | SUNNY |
| 65/52  | 62/42  | 60/48 | 65/55 | 65/54 | 65/54 | 65    |
| POP 0  | POP 0  | POP 0 | POP 0 | POP 0 | POP 0 | POP 0 |

## KENNEDY AIRPORT

|        |        |       |       |       |       |       |
|--------|--------|-------|-------|-------|-------|-------|
| PTCLDY | PTCLDY | SUNNY | SUNNY | SUNNY | SUNNY | SUNNY |
| 64/53  | 62/42  | 60/48 | 65/55 | 65/54 | 65/54 | 65    |
| POP 0  | POP 0  | POP 0 | POP 0 | POP 0 | POP 0 | POP 0 |

## LAGUARDIA AIRPORT

|        |        |       |       |       |       |       |
|--------|--------|-------|-------|-------|-------|-------|
| PTCLDY | PTCLDY | SUNNY | SUNNY | SUNNY | SUNNY | SUNNY |
| 65/52  | 62/42  | 60/48 | 65/55 | 65/54 | 65/54 | 65    |
| POP 0  | POP 0  | POP 0 | POP 0 | POP 0 | POP 0 | POP 0 |

## Area Conditions for New York (Manhattan), NY

[↑ Top of page](#)
[↑ Table of contents for New York \(Manhattan\), NY](#)

ASUS41 KPHL 160915  
SWRNJ

## REGIONAL WEATHER ROUNDUP

## NATIONAL WEATHER SERVICE MOUNT HOLLY NJ

500 AM EDT TUE OCT 16 2001

NOTE: "FAIR" INDICATES FEW OR NO CLOUDS BELOW 12,000 FEET WITH NO SIGNIFICANT WEATHER AND/OR OBSTRUCTIONS TO VISIBILITY.

\* = STATION DOES NOT REPORT PRECIPITATION (E.G. RAIN, SNOW, ETC.) OR FOG.

PAZ001-021-NYZ056-072-MDZ011-DCZ001-161000-

## OTHER NEARBY LOCATIONS

| CITY          | SKY/WX | TMP | DP | RH | WIND | PRES   | REMARKS |
|---------------|--------|-----|----|----|------|--------|---------|
| PITTSBURGH    | MOCLDY | 46  | 40 | 79 | E5   | 29.97F |         |
| ERIE          | CLOUDY | 49  | 43 | 80 | E5   | 30.02F |         |
| BINGHAMTON    | CLEAR  | 40  | 37 | 89 | SE8  | 30.15F | WCI 34  |
| NEW YORK CITY | CLEAR  | 53  | 48 | 83 | E5   | 30.21S |         |
| BALTIMORE     | CLEAR  | 44  | 42 | 93 | CALM | 30.15F |         |
| WASHINGTON DC | CLEAR  | 53  | 50 | 89 | CALM | 30.15F |         |
